




YOUR LB FUNDS AT WORK

# Alley Management Plan

Citywide  
Long Beach, CA

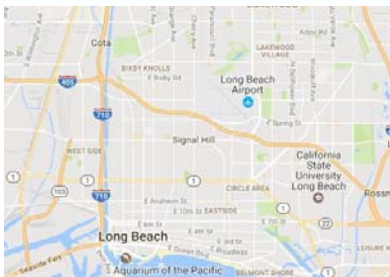

## PROJECTED TIMELINE

Current Phase:  
N/A

Percent Complete:  
50%

Planning:  
N/A

Design:  
N/A

BID/Award:  
N/A

Construction:  
N/A

Completion:  
Anticipated Fall 2017

Measure A funds are being used to assess all of the City's approximate 220 miles of alleys. An assessment has been conducted and the information is being incorporated into the City's Pavement Management Plan (PMP). The plan will define the alleys with the highest priority needs and prescribe the most efficient techniques to improve overall alley condition citywide.

## Project Funding, FY 17:

Measure A: \$300,000

Other Funding: N/A

Total: \$300,000

## All sources as a % of project funding:



CITY OF  
**LONG BEACH**



**YOUR LB FUNDS AT WORK**



## PROJECTED TIMELINE

Current Phase:  
Design

Percent Complete:  
10%

Planning:  
Complete

Design:  
Aug. 2017

BID/Award:  
N/A

Construction:  
Anticipated Spring 2018

Completion:  
Anticipated Summer 2018

# Arterial Street

Broadway from  
Alamitos Ave. to  
Redondo Ave.

Long Beach,  
90802-90803

Improvements and rehabilitation will be made to major arterial streets citywide based on greatest need. Broadway, from Alamitos Ave. to Redondo Ave., has been identified as the first to receive repair. Improvements will include constructing cement concrete curbs, gutters, and sidewalk; new asphalt pavement, traffic striping, signage, and curb painting.


## Project Funding, FY 17:

Measure A: \$4,840,000


Other Funding: N/A

Total: \$4,840,000


## All sources as a % of project funding:

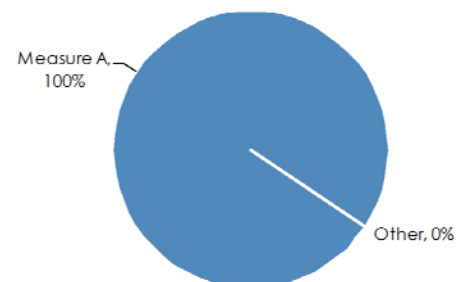

CITY OF  
**LONG BEACH**

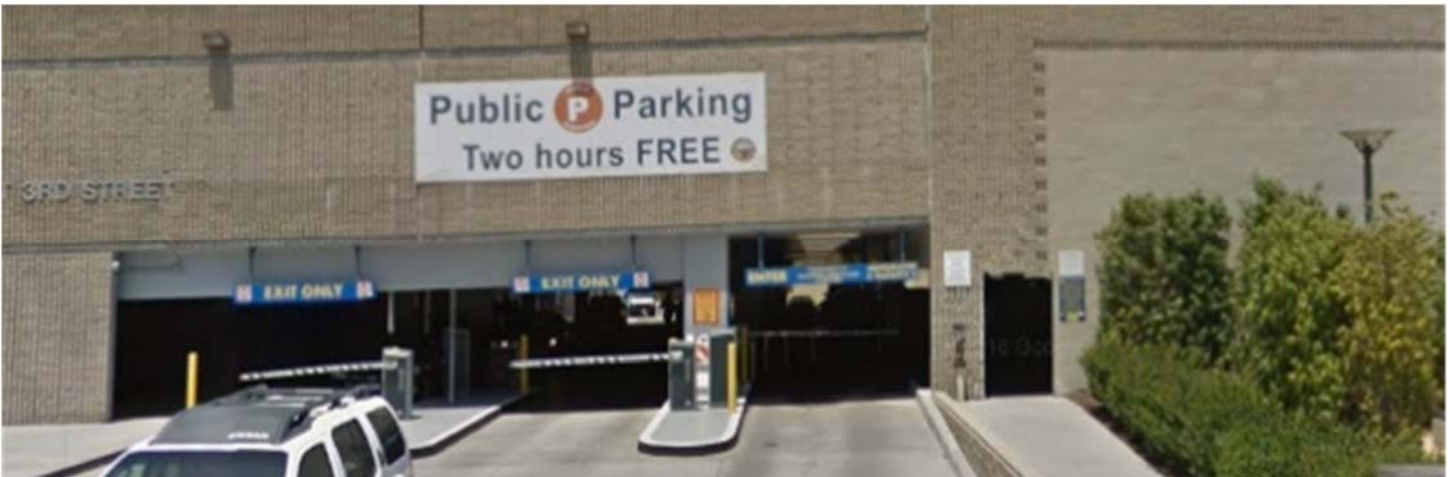

YOUR LB FUNDS AT WORK



## PROJECTED TIMELINE

Current Phase:  
Design

Percent Complete:  
20%

Planning:  
Complete

Design:  
In Progress

BID/Award:  
N/A

Construction:  
November 2017

Completion:  
Anticipated Feb. 2018

# City Place Parking Garage

51 E. 3rd Street  
Long Beach, 90802

Enhancements will be made to the City Place Parking Garage to improve ADA access and pedestrian improvements to the Harvey Milk Park entrance. Improvements include eliminating “nooks” behind stairs, widening of pedestrian entrance/exit to Pine Ave., and fresh interior paint. Future upgrades may include wayfinding signage, façade improvements, and artwork throughout the structure. Additional efforts closely coordinated through this project include installation of Electrical Vehicle charging stations, solar panels, security cameras, and improved pedestrian connections.


## Project Funding, FY 17:

Measure A: \$1,200,000

Other Funding: N/A

Total: \$1,200,000

## All sources as a % of project funding:



CITY OF  
**LONG BEACH**






**YOUR LB FUNDS AT WORK**

# Naples Bridge

E. 2nd Street  
Long Beach, 90803

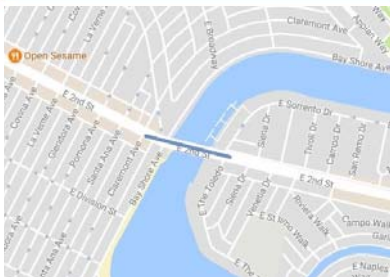

## PROJECTED TIMELINE

Current Phase:  
Construction

Percent Complete:  
30%

Planning:  
Complete

Design:  
Complete

BID/Award:  
Complete

Construction:  
August 2017

Completion:  
Anticipated Aug. 2017


## Project Funding, FY 17:

Measure A: \$100,000

Other Funding: N/A

Total: \$100,000

## All sources as a % of project funding:



CITY OF  
**LONG BEACH**



# Residential Streets

Citywide  
Long Beach, CA

YOUR LB FUNDS AT WORK



Repairs and rehabilitation will be made to existing residential streets and sidewalks citywide. Rehab work will include ADA-compliant curb ramps as well as asphalt slurry, curbs, gutters and concrete work. Street improvements are taking place in all council districts across the city.

## PROJECTED TIMELINE

Current Phase:  
Construction

Percent Complete:  
80%

Planning:  
Complete

Design:  
Completed Sept. 2016

BID/Award:  
N/A

Construction:  
Jan. 2017

Completion:  
Anticipated Fall 2017


## Project Funding, FY 17:

Measure A: \$11,080,000

Other Funding: \$4,500,000

Total: \$15,580,000

## All sources as a % of project funding:

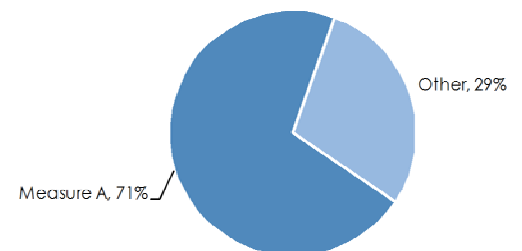


CITY OF  
**LONG BEACH**



YOUR LB FUNDS AT WORK

# Street Signage

Citywide  
Long Beach, CA

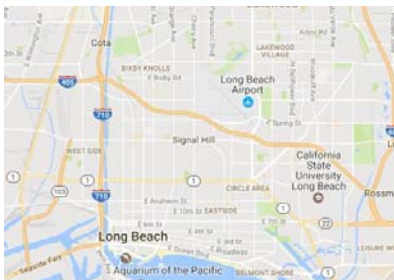

## PROJECTED TIMELINE

Current Phase:  
Installation

Percent Complete:  
10%

Planning:  
Complete

Design:  
N/A

BID/Award:  
N/A

Construction:  
N/A


Completion:  
Anticipated Fall 2017

Measure A Funds will be used to replace street signage in the city. The Citywide Signage Program is responsible for the installation and replacement of street name signs and traffic control signs at various locations throughout the city. Measure A funds provide for the purchase, replacement and installation of traffic, regulatory, and street sweeping signs, citywide.

### Project Funding, FY 17:

Measure A: \$50,000  
Other Funding: N/A  
Total: \$50,000

### All sources as a % of project funding:



CITY OF  
**LONG BEACH**
